

Package No	Description of Procurement package Goods	Unit	Quantity	Procurement Method & Type	Contract Approving Authority	Source of Funds	Estd. Cost in Million Tk.	Time Code for Process	Advertise Prequel (if applicable)	Invite/Advertisement Tender	Tender Opening	Tender Evaluation	Approval to Award	Notification of Award	Signing of Contract	Total Time to Contract Signature	Time for Completion of Contract (from the date of signing the contract)				
GD-14 (Lot-02)	২০ ইঞ্চি কাটার সাবসন ডেকোর	টি	৪	এটিএম (স্বাইসিটি)	মিরাজিপি	জিএস	১২১.১৫	Actual Dates		১৭/০৭/২০২২	৩১/০৮/২০২২	২৮/০৮/২০২২	২৮/১১/২০২২	৫/১২/২০২২	৩/১২/২০২২	১৬৮	২৪ মাস/৭২০ দিন				
	২০" কাটার সাবসন ডেকোরের জন্য এইচডিপিই ড্রাইং পাইপ	মিঃ	৩৯০০				১৪২.৬৫	Planned Days		৪৫											
	২০" কাটার সাবসন ডেকোরের জন্য ফেয় টাইপ ড্রাইং	টি	১৩০০				১৯৬.৯৯														
	২০ ইঞ্চি কাটার সাবসন ডেকোরের জন্য এন সোর পাইপ	মিঃ	৬০০				১৫৩.৭৫														
	২০ ইঞ্চি কাটার সাবসন ডেকোরের জন্য কল্ডফর্মিট সাবসন ডেকোরের জন্য	মিঃ	৪৫০০				১৬৪.৫৯														
	২০" কাটার সাবসন ডেকোরের জন্য সকেট	টি	১০০				১২৫.৪০														
	২০" কাটার সাবসন ডেকোরের রানার বোল্ড পাইপ	টি	২০০				৫৭.৪৮														
	২০" কাটার সাবসন ডেকোরের জন্য খুচরা যন্ত্রাংশ	থাক	-				১০৪.৫০														
	২০" কাটার সাবসন ডেকোরের ডেম-রাট	টি	৪				৪০.৭০														
	২০" কাটার সাবসন ডেকোরের ডেম-রাটের খুচরা যন্ত্রাংশ	থাক	-				২০.৯০														
GD-15 (Lot-01)	১৮ ইঞ্চি কাটার সাবসন ডেকোর	টি	৩	এটিএম (স্বাইসিটি)	মিরাজিপি	জিএস	২৬৮৩.০০	Actual Dates		২৬/০৪/২০২২	১৪/০৬/২০২২	১৪/০৭/২০২২	১৪/০৮/২০২২	২৬/০৮/২০২২	২৪/১০/২০২২	১৮৮	১৮ মাস/৫৪০ দিন				
	১৮" কাটার সাবসন ডেকোরের জন্য এইচডিপিই ড্রাইং পাইপ	মিঃ	২,৯৮৮				৯০.৬৭	Planned Days		৫৪											
	১৮" কাটার সাবসন ডেকোরের জন্য ফেয় টাইপ ড্রাইং	টি	৯৯৬				১৩৫.৩১														
	১৮ ইঞ্চি কাটার সাবসন ডেকোরের জন্য এন সোর পাইপ	মিঃ	৩০০০				৬২.৭০														
	২০ ইঞ্চি এক ১৮ ইঞ্চি কাটার সাবসন ডেকোরের জন্য কল্ডফর্মিট সাবসন ডেকোরের জন্য	মিঃ	৩০০০				১০৯.৭২														
	১৮" কাটার সাবসন ডেকোরের জন্য সকেট	টি	৬০				৬২.৭০														
	১৮" কাটার সাবসন ডেকোরের রানার বোল্ড পাইপ	টি	৯০				২০.৫৩														
	১৮" কাটার সাবসন ডেকোরের জন্য খুচরা যন্ত্রাংশ	থাক	-				৬২.৭০														
	২০" , ১৮" এক ১২" কাটার সাবসন ডেকোরের ডেম-রাট	টি	৩				৩০১.২৮														
	২০" , ১৮" এক ১২" কাটার সাবসন ডেকোরের ডেম-রাটের খুচরা যন্ত্রাংশ	থাক	-				১৫.৬৮														
GD-15 (Lot-02)	উপসেট-পারফেক্ট-১৫ (৪টি-০১)	করণ	৬৭	এটিএম (স্বাইসিটি)	মিরাজিপি	জিএস	১৬৮৬.৮৩	Actual Dates		২৬/০৪/২০২২	১৪/০৬/২০২২	১৪/০৭/২০২২	১৪/০৮/২০২২	২৬/০৮/২০২২	২৪/১০/২০২২	১৮৮	১৮ মাস/৫৪০ দিন				
	১৮ ইঞ্চি কাটার সাবসন ডেকোর	টি	৩				৯০.৬৭	Planned Days		৫৪											
	১৮" কাটার সাবসন ডেকোরের জন্য এইচডিপিই ড্রাইং পাইপ	মিঃ	২,৯৮৮				১৩৫.৩১														
	১৮" কাটার সাবসন ডেকোরের জন্য ফেয় টাইপ ড্রাইং	টি	৯৯৬				৬২.৭০														

Package No	Description of Procurement package Goods	Unit	Quantity	Procurement Method & Type	Contract Approving Authority	Source of Funds	Estd. Cost in MillionTk.	Time Code for Process	Advertise Prequel (if applicable)	Invite/Advertisement Tender	Tender Opening	Tender Evaluation	Approval to Award	Notification of Award	Signing of Contract	Total Time to Contract Signature	Time for Completion of Contract (from the date of signing the contract)	
GD-15 (Lot-03)	২০৫ এক ১৮ কটির সাফলন ডেকোরের জন্য কলিনকিট সাফারাইলিন পাইপ	মিঃ	৩০০০			জিএম	১০৯.৭২											
	১৮" কটির সাফলন ডেকোরের জন্য সকেট	কোয়ালি	৬০				৬২.৭০											
	১৮" কটির সাফলন ডেকোরের রানার বোল্ড পাইপ	টি	৯০				২৩.৫৩											
	গ্লাস পাল্প (১৮" কটির সাফলন ডেকোরের জন্য)	টি	১				৭৮.৩৮											
	১৮" কটির সাফলন ডেকোরের জন্য খুচরা খয়াল সাফার।	বোকার	-				৬২.৭০											
	২০", ১৮" এক ১২" কটির সাফলন ডেকোরের ডেনেকোট	টি	৩				৩০.২৮											
	২০", ১৮" এক ১২" কটির সাফলন ডেকোরের ডেনেকোটের খুচরা খয়াল সাফার	বোকার	-				১৫.৬৮											
	এক এক খয়াল বোল্ড (বিল্ডিং সাইজের) (প্রতি কয়েক ৩০০ মিটার)	কয়েক	৬৭				১৩.৯৩											
	উপরেটি-পারকোজ-১৫ (লিট-০২)						১৭৫.২১											
	১৮" কটির সাফলন ডেকোর	টি	৩				৩০৫.৬১	Actual Dates		২৬/০৪/২০২২	১৯/০৬/২০২২	১৯/০৭/২০২২	১৯/০৮/২০২২	২৬/০৯/২০২২	২৮/১০/২০২২	১৭৮	১৮ মাস/৫৪০ দিন	
১৮" কটির সাফলন ডেকোরের জন্য এইচডিপিই প্রোডিং পাইপ	মিঃ	২,৯৮৮				৯০.৬৭	Planned Days			৫৪		২৯	৬০	৭	২৮			
১৮" কটির সাফলন ডেকোরের জন্য খয়াল টাইপ প্রোট	টি	৯৯৬				১০৫.৩১												
১৮ কটির সাফলন ডেকোরের জন্য এক মোর পাইপ	মিঃ	৩০০০.০০				৬২.৭০												
২০৫ এক ১৮ কটির সাফলন ডেকোরের জন্য কলিনকিট সাফারাইলিন পাইপ	মিঃ	৩০০০.০০				১০৯.৭২												
১৮" কটির সাফলন ডেকোরের জন্য সকেট	কোয়ালি	৬০.০০				৬২.৭০												
১৮" কটির সাফলন ডেকোরের রানার বোল্ড পাইপ	টি	৯০.০০				২৩.৫৩												
১৮" কটির সাফলন ডেকোরের জন্য খুচরা খয়াল সাফার।	বোকার	-				৬২.৭০												
২০", ১৮" এক ১২" কটির সাফলন ডেকোরের ডেনেকোট	টি	৩				৩০.২৮												
২০", ১৮" এক ১২" কটির সাফলন ডেকোরের ডেনেকোটের খুচরা খয়াল সাফার	বোকার	-				১৫.৬৮												
এক এক খয়াল বোল্ড (বিল্ডিং সাইজের) (প্রতি কয়েক ৩০০ মিটার)	কয়েক	৬৬				১৩.৯৩												
উপরেটি-পারকোজ-১৫ (লিট-০৩)						১৬৮.৮৩												
১২ ইঞ্চি কটির সাফলন ডেকোর	টি	২				২৫৮.২৩	Actual Dates		৫/১২/২০২২	২৮/০৬/২০২২	৭/২৬/২০২২	৯/২৬/২০২২	৯/২৬/২০২২	১০/১/২০২২	১০/০০/২০২২	১৭১	১৮ মাস/৫৪০ দিন	
১২" কটির সাফলন ডেকোরের জন্য এইচডিপিই প্রোডিং পাইপ	মিঃ	৩৯৯৬				১০০.২৩	Planned Days			৪৭		২৮	৬১	৭	২৮			
১২" কটির সাফলন ডেকোরের জন্য খয়াল টাইপ প্রোট	টি	১৩৩২				১৬৭.০৩												
১২ কটির সাফলন ডেকোরের জন্য এক মোর পাইপ	মিঃ	৬০০০				৯৪.০৫												
১২" কটির সাফলন ডেকোরের জন্য সকেট	টি	২০				১৬.৭২												
১২" কটির সাফলন ডেকোরের রানার বোল্ড পাইপ	টি	৫০				১০.৪৫												
১২" কটির সাফলন ডেকোরের জন্য খুচরা খয়াল সাফার।	বোকার	-				২০.৯০												
২০", ১৮" এক ১২" কটির সাফলন ডেকোরের ডেনেকোট	টি	৮				৮০৩.৪০												
২০", ১৮" এক ১২" কটির সাফলন ডেকোরের ডেনেকোটের খুচরা খয়াল সাফার	বোকার	-				৪১.৮০												

Package No	Description of Procurement package Goods	Unit	Quantity	Procurement Method & Type	Contract Approving Authority	Source of Funds	Estd. Cost in Million Tk.	Time Code for Process	Advertiser Prequal (if applicable)	Invite/Advertisement Tender	Tender Opening	Tender Evaluation	Approval to Award	Notification of Award	Signing of Contract	Total Time to Contract Singnature	Time for Completion of Contract (from the date of signing the contract)
	এক্স-এন এনার রোল (পলিথিন সাইডের) (এটি করেণ ৩০০ মিটার)	করপন	৫০				১০.৪৫										
	উপসোর্ট-প্যাকেজ-১৬																
GD-17 Lot-01	ড্রেইপিং সাকশন রোপার ডেকোর (রোপার কাপাশিটি ১১০০ ফারিটার/মিটা)	টি	১	ওটিএম (আইসিটি)	ফিনিজিং	কির্দরি	১৫২০.২৬			২০/০৭/২০২২	০৪/০৮/২০২২	০২/১০/২০২২	০১/১১/২০২২	০৪/১২/২০২২	০৫/০১/২০২৩	১৬	১৮ মাস/৫৪০ দিন
	ড্রেইপিং সাকশন রোপার ডেকোর (রোপার কাপাশিটি ১১০০ ফারিটার/মিটা) এর জন্য খুঁচরা ম্যানেশন সফট						৩১.৩৫				৪৬	২৮	৩০	৭	২৮	১৬৯	
	উপসোর্ট-প্যাকেজ-১৭ (লট-১)																
GD-17 Lot-02	ড্রেইপিং সাকশন রোপার ডেকোর (রোপার কাপাশিটি ২০০০ ফারিটার/মিটা)	খোক	-	ওটিএম (আইসিটি)	ফিনিজিং	কির্দরি	২২৬২.২৩			১০/০১/২০২১	১/১০/২০২২	১০/০২/২০২২	১১/০৪/২০২২	১৪/০৪/২০২২	১৬/০৫/২০২২	২৪৫	১৮ মাস/৫৪০ দিন
	ড্রেইপিং সাকশন রোপার ডেকোর (রোপার কাপাশিটি ২০০০ ফারিটার/মিটা) এর জন্য খুঁচরা ম্যানেশন সফট						৫২.২৫				১২২	২৮	৬০	৭	২৮	২৪৫	
	উপসোর্ট-প্যাকেজ-১৭ (লট-২)																
GD-18	ওগাটার ইনজেকশন/কোটিং ডেকোর	টি	২	ওটিএম (আইসিটি)	মৌলিকরকন ম্যানেশন	কির্দরি	২৩১৪.৪৮			২৭/৭/২০২২	৪/৮/২০২২	১০/৬/২০২২	০৫/১২/২০২২	১২/১২/২০২২	১/১/২০২৩	১৬৬	১২ মাস/৩৬৫ দিন
	ওগাটার কোটিং/ইনজেকশন ডেকোর (কো মনাতম ৪০০০ ফারিটার/মিটা) এর জন্য খুঁচরা ম্যানেশন সফট						৩১.৩৫				৪০	২৮	৬০	৭	২৮	১৬৬	
	উপসোর্ট-প্যাকেজ-১৮																
GD-19 (Lot-02)	চোপ ধরপত মনুন মাউন্ট এন ডেকোর (স্পরেশ কেরি বার্কস)	টি	১	ওটিএম (আইসিটি)	ফিনিজিং	কির্দরি	১১১০.১৮			২৭/৭/২০২২	৪/৮/২০২২	১০/৬/২০২২	০৫/১২/২০২২	১২/১২/২০২২	১/১/২০২৩	১৬৬	১৮ মাস/৫৪০ দিন
	উপসোর্ট-প্যাকেজ-১৯ (লট-২)																
GD-20 (Lot-01)	সারভ জার্কেন্টেট (ক্রাটিকোরিন টাইপ)	টি	৬	ওটিএম (আইসিটি)	মৌলিকরকন ম্যানেশন	কির্দরি	২০২২.৩৩			০১/০৮/২০২২	৩১/০৮/২০২২	৩১/১৮/২০২২	১১/১২/২০২২	১১/১২/২০২২	১৭/১২/২০২২	১৬৬	
	সারভ জার্কেন্টেট (ক্রাটিকোরিন টাইপ) এর জন্য খুঁচরা ম্যানেশন সফট						৪০৫.০০				৪০	২৮	৬০	৭	২৮	১৬৬	
	ইনজেকশন স্পরেশ	টি	৪				১১০.০০				৩০	২৮	৬০	৭	২৮	১৬৬	
	উপসোর্ট-প্যাকেজ-২০																
GD-21 (Lot-2)	ডাইক নিম্বোর জন্য রবার টিউব	টি	১০	ওটিএম (আইসিটি)	মৌলিকরকন ম্যানেশন	কির্দরি	১৩২.০০			৮/৩০/২০২২	৪/১২/২০২২	১০/২৭/২০২২	১২/১১/২০২২	১২/১৮/২০২২	১/১৫/২০২৩	১৩৮	১৫ মাস/৪৫০ দিন
	উপসোর্ট-প্যাকেজ-২১ (লট-২)																
GD-22	ড্রেইপিং সাকশন রোপার ডেকোর	টি	২	ওটিএম (আইসিটি)	সম্মার নিরীক্ষা ধরন	কির্দরি	২০০.০০			৪/১/২০২২	১০/২/২০২২	১০/৩০/২০২২	১১/১৪/২০২২	১২/১৮/২০২২	১/১৫/২০২৩	১০৯	১২ মাস/৩৬৫ দিন
	ড্রেইপিং সাকশন রোপার ডেকোর						২০০.০০				৩১	২৮	১৫	৭	২৮	১০৯	
	Total value of goods procurement						২১৮৬৬.১৯										



সংশ্লিষ্ট অফিসের সাক্ষর

**Annual Procurement Plan &
Procurement Implementation Report (2022-2023)**

Ministry/Division : Ministry of Shipping

Agency : Bangladesh Inland Water Transport Authority (BIWTA)

Procuring Entity Name & Code : Bangladesh Inland Water Transport Authority (BIWTA)

Project/Programme Name & Code : Modernization of River Port including allied facilities at Paturia and Daulatdia & Code 224320000

Package No.	Description of Procurement Package SERVICES	Unit	Quantity	Procurement Method & Type	Contract Approving Authority	Source of Funds	Estimated Cost in Million Tk.	Time Code for Process	Avestise EOI	Issue RFP	Technical Proposal opening	Technical Proposal Evaluation	Financial Proposal opening & Evaluation	Negotiation	Approval	Signing of Contract	Total time to Contract Signature	Time for Completion of Contract	
01	02	03	04	05	06	07	08	09	10	11	12	13	14	15	16	17	18	19	
Not Applicable																			
								Planned Dates											
								Planned Dates											
								Actual Dates											

Handwritten signature

**Ann Annual Procurement Plan &
Procurement Implementation Report (2022-2023)**

Budget : Development

Ministry/Division : Ministry of Shipping
 Agency : Bangladesh Inland Water Transport Authority (BIWTA)
 Procuring Entity Name & Code : Bangladesh Inland Water Transport Authority (BIWTA)
 Project/Programme Name & Code : Modernization of River Port including allied facilities at Paturia and Dauladia & Code 224320000

Package No.	Description of Procurement Package GOODS	Unit	Quantity	Procurement Method & Type	Contract Approving Authority	Source of Funds	Estimated Cost in Million Tk.	Time Code for Process	Not Used in Goods	Invite/ Advertise Tender	Tender Opening	Tender Evaluation	Approval to Award	Notification of Award	Signing of Contract	Total time to Contract Signature	Time for Completion of Contract	
01.	Procurement of Terminal Pontoon with shed under the Project "Modernization of river port including allied facilities at Paturia and Dauladia."	--	06 Nos.	OTM	MoS	GOB	89.999	Planned Dates Planned Days		28.11.21 28	26.12.21 21	16.01.22 14	30.01.22 7	06.02.22 14	20.02.22 120	20.06.22 84	--	
02.	Procurement of Speed boat & Engine boat pontoons with shed under the Project "Modernization of river port including allied facilities at Paturia and Dauladia."	--	04 Nos.	OTM	MoS	GOB	59.998	Planned Dates Planned Days		30.11.21 28	29.12.21 21	18.01.22 14	01.02.22 7	08.02.22 14	22.02.22 120	22.06.22 84	--	
03.	Procurement of Ro-Ro ferry pontoon including 2 nos 40 feet long ramp under the Project "Modernization of river port including allied facilities at Paturia and Dauladia."	--	04 Nos.	OTM	MoS	GOB	214.808	Planned Dates Planned Days		03.02.22 29	07.03.22 21	26.04.22 35	22.02.22 07	01.05.22 14	11.09.22 --	--	--	
04.	Procurement of Ro-Ro ferry pontoon including 2 nos 40 feet long ramp under the Project "Modernization of river port including allied facilities at Paturia and Dauladia."	--	04 Nos.	OTM	MoS	GOB	214.808	Planned Dates Planned Days		30.11.21 28	28.12.21 21	18.01.21 35	22.02.22 7	01.03.22 14	11.09.22 180	--	--	
05.	Procurement of Utility ferry pontoon including 40 feet long ramp under the Project "Modernization of river port including allied facilities at Paturia and Dauladia."	--	04 Nos.	OTM	MoS	GOB	90.383	Planned Dates Planned Days		30.11.21 28	28.12.21 21	18.01.21 14	22.02.22 7	01.03.22 14	11.09.22 180	84	--	
Total Value of Goods Procurement :							669.996											

**Annual Procurement Plan &
Procurement Implementation Report (2022-2023)**

Budget : Development

Ministry/Division : Ministry of Shipping
 Agency : Bangladesh Inland Water Transport Authority (BIWTA)
 Procuring Entity Name & Code : Bangladesh Inland Water Transport Authority (BIWTA)
 Project/Programme Name & Code : Modernization of River Port including allied facilities at Paturia and Daulatdia & Code 224320000

Package No.	Description of Procurement Package WORKS	Unit	Quantity	Procurement Method & Type	Contract Approving Authority	Source of Funds	Estimated Cost In Million Tk.	Time Code for Process		Advertise Prequel (if applicable)	Invite/ Advertise Tender	Tender Opening	Tender Evaluation	Approval to Award	Notification of Award	Signing of Contract	Total time to Contract Signature	Time for Completion of Contract
								09	10									
01.	Site Development by carried earth including cutting, filling, leveling, dressing and compaction in Paturia Ghat area.	m ³	2.76 L m ³	OTM	--	GOB	109.521	Planned Dates	01.12.21		28	29.12.21	16.01.22	02.02.22	06.02.22	23.02.22	23.06.22	--
								Planned Dates	03.02.22									
								Actual Dates	06.03.22									
02.	Site Development by carried earth including cutting, filling, leveling, dressing and compaction in Daulatdia Ghat area.	m ³	1.88 L m ³	OTM	--	GOB	80.00	Planned Dates	01.12.21		28	29.12.21	16.01.22	02.02.22	06.02.22	23.02.22	23.06.22	--
								Planned Dates	03.02.22									
								Actual Dates	06.03.22									
03.	Land acquisition: a) Paturia b) Daulatdia	L.S	35 acre 30 acre	--	--	GOB	560.00 360.00 920.00	Planned Dates										
								Planned Dates										
								Actual Dates										
Total Value of WORKS Procurement :								1109.521										

Signature
26/05/2022

মোহাম্মদ তারিকুল হাশান
 তত্ত্বাবধায়ক এককোশলী (পূর্ব)
 ও একক পরিচালক
 বাসায়োসক, ঢাকা।

ANNUAL PROCUREMENT PLAN FY: 2022-23 (GOODS)

Ministry/Division :		Ministry of Shipping		Project Cost (in Lakh Taka)		Approval of Revised DPP		8 Nov-2020											
Implementing Agency :		Ministry of Shipping		Total		334,942.00		31 Dec-2025											
Procuring Entity Name & Code :		Bangladesh Inland Water Transport Authority (BIWTA) & 131016600		GOB		29,662.00		Updated as on											
Project/Program Name & Code :		Bangladesh Regional Waterway Transport Project-I(IDA Credit No. 5842-BD) & 224091900		PA		305,280.00		18 Nov-2020											
BRWTP-Package#	Description of Procurement Package (Goods)	Unit	Quantity	Procedure Method/ Type	Contract Approving Authority *	Source of Fund	Estimated Cost in Lakh Taka	Time Code for Process	Invite/Advertisement of Tender	Tender Opening	Tender Evaluation	Approval To Award	Notification of Award	Signing of Contract/PO	Total Time to Contract signing (days)	Time for Completion of Contract	Progress		
1	GOODS	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18		
G2	Procurement of hydrographic survey and related equipment.	Lot	3	OTM/ICB	BIWTA	IDA	2,500.00	Planned Date Planned Days Actual Date	Jul-2022 45 	Aug-2022 45 	Nov-2022 90 	Nov-2022 15 	Dec-2022 7 	Dec-2022 21 	178 	Dec-2023 365 			
G3	Modern teaching aids and equipment including computers, bridge and navigation simulators, workshop machinery, life saving items and other	Lot	1	OTM/NCB	PD	IDA	2,200.00	Planned Date Planned Days Actual Date	Sep-2022 45 	Oct-2022 45 	Jan-2023 90 	Jan-2023 15 	Feb-2023 7 	Feb-2023 21 	178 	Feb-2024 365 			
G9	Equipment for Hydrological Server system and Data Storage	Lot	1	OTM/NCB	PD	IDA	100.00	Planned Date Planned Days Actual Date	Aug-2022 45 	Sep-2022 45 	Dec-2022 90 	Dec-2022 15 	Jan-2023 7 	Jan-2023 21 	178 	Jan-2024 365 			
G12	Material Handling Equipment (Cranes, Pneumatic unloader, Bagging machine and Ground handling equipment) for Pangaon & Ashganj Cargo	Lot	2	OTM/NCB	MINISTRY	IDA	5,500.00	Planned Date Planned Days Actual Date	Jan-2023 30 	Jan-2023 30 	May-2023 90 	May-2023 15 	May-2023 7 	Jun-2023 21 	163 	Jun-2024 365 			
Total for Goods							4,700.00												
Total value of Goods Procurement							2,200.00												

(Signature)

(Signature)

(A.H. Md. Farhad Uzzaman)
Deputy Project Director
BRWTP-1 Project
BIWTA, Dhaka.

Md. Ayub Ali
Project Director
BRWTP-1 Project
BIWTA, Dhaka.

REVISED ANNUAL PROCUREMENT PLAN FY: 2022-23 (WORKS)

Ministry/Division :		Ministry of Shipping																	
Implementing Agency :		Bangladesh Inland Water Transport Authority (BIWTA)																	
Procuring Entity Name & Code :		Bangladesh Inland Water Transport Authority (BIWTA) & 131016600																	
Project/Program Name & Code :		Bangladesh Regional Waterway Transport Project-1(IDA Credit No. 5842-BD) & 224091900																	
BRWTP-Package#	Description of Procurement Package (Works)	Unit	Quantity	Procedure Method/ Type	Contract Approving Authority	Source of Fund	Estimated Cost in Lakh Taka	Itemwise cost (Taka)	Time Code for Process	Invite/Advertisement of Tender	Tender Opening	Tender Evaluation	Project Cost (in Lakh Taka)			Approval of Revised DPP	Closing Date of Project	Time for Completion of Contract	Progress
													Total	GOB	PA				
													334942.00	29662.00	305280.00	8 Nov-2020	31 Dec-2025	Updated 18-Nov-20	
													COB	PA					
													Approval To Award	Notification of Award	Signing of Contract/PO	Total Time to Contract signing	Time for Completion of Contract		
													13	14	15	16	17		
													18						
													19						
													20						
													21						
													22						
													23						
													24						
													25						
													26						
													27						
													28						
													29						
													30						
													31						
													32						
													33						
													34						
													35						
													36						
													37						
													38						
													39						
													40						
													41						
													42						
													43						
													44						
													45						
													46						
													47						
													48						
													49						
													50						
													51						
													52						
													53						
													54						
													55						
													56						
													57						
													58						
													59						
													60						
													61						
													62						
													63						
													64						
													65						
													66						
													67						
													68						
													69						
													70						
													71						
													72						
													73						
													74						
													75						
													76						
													77						
													78						
													79						
													80						
													81						
													82						
													83						
													84						
													85						
													86						
													87						
													88						
													89						
													90						
													91						
													92						
													93						
													94						
													95						
													96						
													97						
													98						
													99						
													100						

(A.H. Md. Farhad Uzzaman)
Deputy Project Director
BRWTP-1 Project
BIWTA, Dhaka.

Md. Ayub Ali
Project Director
BRWTP-1 Project
BIWTA, Dhaka.

NON CONSULTANCY SERVICE (NCS)															
NCS1	Procurement/Outsourcing of Crews & Staffs (Master-2/Driver-2/Q/Master-3, Officer cook-2, Greaser-4, Laskor-4, Topash-2, Vendery-2) total 21 persons for operation of 2 nos survey/Inspection vessel	pm	48 (for each crew/staff)	N/C/B/OTM	PD	IDA	247.00	Planned Dates	Sep-2022	Nov-2022	Feb-2023	Feb-2023	Feb-2023	Mar-2023	Mar-2024
NCS2	Biodiversity Conservation and Implementation along the IWT Corridor	LS	1	N/C/B/OTM	PD	IDA	1300.00	Actual Date	Jan-2023	Feb-2023	May-2023	May-2023	Jun-2023	Jun-2023	Jun-2024
Total for Works							70,738.55								



(A.H. Md. Farhad Uzzaman)
 Deputy Project Director
 BRWTP-1 Project
 BIWTA, Dhaka.



Md. Ayub Ali
 Project Director
 BRWTP-1 Project
 BIWTA, Dhaka

REVISED ANNUAL PROCUREMENT PLAN FY: 2022-23 (SERVICES)

Ministry/Division :	Ministry of Shipping	Project Cost (in Lakh Taka)	334,942,000	Approval of Revised DPP	8 Nov-2020
Implementing Agency :	Bangladesh Inland Water Transport Authority (BIWTA)	Total	334,942,000	Closing Date of Project	31 Dec-2025
Procuring Entity Name & Code :	Bangladesh Inland Water Transport Authority (BIWTA) & 131016600	GOB	29,662,000	Updated as on	18 Nov-2020
Project/Program Name & Code :	Bangladesh Regional Waterway Transport Project-1 (IDA Credit No. 5842-BD) & 224091900	PA	305,280,000		

BRWTP_Package#	Description of Procurement Package of Services	Unit	Quantity	Procedure Method/Type	Contract Approving Authority*	Source of Fund	Estimated Cost in Lakh Taka	Time Code for Process		Advertise- EOI	Issue RFP	Proposal Opening	Proposal Evaluation	Financial Proposal Opening & Evaluation	Negotiation	Approval	Signing of Contract	Total Time to Contract Signature (days)	Time for Completion of Contract	Progress
								9	10											
SERVICES (Firm)																				
1	S 7	Design and Development of System to prepare and disseminate Hydrographic Information Electronically	pmm	10	FBS/OP EN INTERN ATIONA L	PD	IDA	400.00	Planned Dates	Feb-2021	Jun-2021	Jul-2021	Aug-2021	Aug-2021	Sep-2021	Oct-2021	18-Oct-21	260	900.00	REOI evaluation ongoing
									Planned Dates	Feb-2021	Jun-2021	Jul-2021	Aug-2021	Aug-2021	Sep-2021	Oct-2021	18-Oct-21	260	900.00	
									Actual Dates	8-Feb-22										
2	S 9/2	Training needs assessment/study and action plan development for establishing /supporting training institutions for inland water transport sector.	pmm	10	QCBS/O PEN INTERN ATIONA L	PD	IDA	400.00	Planned Dates	Feb-2021	Jun-2021	Jul-2021	Aug-2021	Aug-2021	Sep-2021	Oct-2021	18-Oct-21	260	900.00	REOI evaluation ongoing
									Planned Dates	Feb-2021	Jun-2021	Jul-2021	Aug-2021	Aug-2021	Sep-2021	Oct-2021	18-Oct-21	260	900.00	
									Actual Dates	16/03/2022										
3	S14/13	Hardware/Networking expert (1 Person)	pmm	48	SIC/OPEN	PD	IDA	150.00	Planned Dates	Aug-2022	Sep-2022	Oct-2022	Nov-2022	Dec-2022	Dec-2022	Jan-2023				REOI evaluation ongoing
									Planned Dates	Aug-2022	Sep-2022	Oct-2022	Nov-2022	Dec-2022	Dec-2022	Jan-2023				
									Actual Dates											
4	S14/18	Software/System Expert (1 person)	pmm	48	SIC/OPEN	PD	IDA	144.00	Planned Dates	Aug-2022	Sep-2022	Oct-2022	Nov-2022	Dec-2022	Dec-2022	Jan-2023				REOI evaluation ongoing
									Planned Dates	Aug-2022	Sep-2022	Oct-2022	Nov-2022	Dec-2022	Dec-2022	Jan-2023				
									Actual Dates											
5	S 15/1	Design and development of AIS (Automatic Identification System) to monitor vessels and Aids to navigation	pmm	6	OBS/OPEN INTERN ATIONA L	PD	IDA	300.00	Planned Dates	1-Jan-21	1-May-21	Jun-2021	Jul-2021	Jul-2021	Aug-2021	Oct-2021	260		REOI evaluation ongoing	
									Planned Dates	1-Jan-21	1-May-21	Jun-2021	Jul-2021	Jul-2021	Aug-2021	Oct-2021	260			
									Actual Dates	9-Feb-22										
Total for Firm							1,394.00													

[Handwritten Signature]
23.08.22

(A.H. Md. Farhad Uzzaman)
Deputy Project Director
BRWTP-1 Project
BIWTA, Dhaka.

[Handwritten Signature]
23.08.2022

(Ma. Ayub Ali)
Project Director
BRWTP-1 Project
BIWTA, Dhaka.

Paka ge no.	Description of Procurement Package Works	Unit	Quantity	Procurement Method & Type	Contract Approving Type	Source of Founds	Estd Cost in Million Tk.	Time Code for Goods		Not Used in Goods	Invite/ Advertise Tender	Tender Opening	Tender Evaluation	Approval to Award	Notificati on of Award	Signing of Contract	Total time to Contract Signature	Time for Completi on of Contract
								Planned Dates	Actual Dates									
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	
Pac-9 Lot-2	Dredging/Digging of Dharala River	Dre = Lakh M ³	23.00	OTM	MOS	GOB	420.00	Planned Dates		26.04.22	26.05.22	18.06.22	19.08.22	26.08.22	30.09.22	-	30.06.24	
Pac-9 Lot-3	Dredging/Digging of Dharala River	Dre = Lakh M ³	23.00	OTM	MOS	GOB	420.00	Planned Dates		26.04.22	26.05.22	18.06.22	19.08.22	26.08.22	30.09.22	147	455	
Pac-9 Lot-4	Dredging/Digging of Dharala River	Dre = Lakh M ³	23.00	OTM	MOS	GOB	420.00	Planned Dates		26.04.22	26.05.22	18.06.22	19.08.22	26.08.22	30.09.22	-	30.06.24	
Pac-5 Lot-2	Performance- Based contract for Improvement (Capital and Maintenance Dredging) of Navigability for Old Brahmaputra ch. 110 km to 117.50 km	Dre = Lakh M ³	30.00	OTM	MOS	GOB	540.00	Planned Dates		26.04.22	26.05.22	18.06.22	19.08.22	26.08.22	30.09.22	147	455	
Pac-5 Lot-5	Performance-Based contract for Improvement (Capital and Maintenance Dredging) of Navigability for Old Brahmaputra ch. 117.50 km to 125 km	Dre = Lakh M ³	35.00	OTM	MOS	GOB	630.00	Planned Dates		26.04.22	26.05.22	18.06.22	19.08.22	26.08.22	30.09.22	147	455	

Const	Construction of office building at Dinajpur	m ²	360.00	OTM	MOS	GOB	90.00	Planned Dates	Planned Dates	Planned Days	Actual Dates	Planned Dates	Planned Days	Actual Dates	-	30.06.24											
								Planned Dates	Planned Dates	Planned Days	Actual Dates	Planned Dates	Planned Days														
Pac-18 Lot-1	Construction of Rubber Dams on Tulai River.	No.	-	OTM	MOS	GOB	200.00	26.07.22	26.08.22	28		18.09.22	21		19.11.22	60		26.11.22	07		30.12.22	31		147		30.06.24	385
Total Value of Procurement Works							4410.00																				

(Handwritten signature)


(রিকিভল ইন্সপেক্টর জেনারেল)
অতিঃ প্রধান প্রকৌশলী (পরি)
৯
প্রকল্প পরিচালক

**ANNUAL PROCUREMENT PLAN &
PROCUREMENT IMPLEMENTATION
REPORT
2022-23**

Budget : Development

Ministry/Division : Ministry of Shipping
Agency : Bangladesh Inland Water Transport Authority (BIWTA)
Procuring Entity Name & Code : Bangladesh Inland Water Transport Authority (BIWTA)
Project/Programme Name & Code : "Construction of Walkway and others allied work on Evicted to the North bank of Dakatia River Shekhatia Bridge to Shuchipara Bridge at Sharasti Upazila in Chandpur District." Code : 2243249.

Package No.	Description of Procurement Package WORKS	Unit	Quantity	Procurement Method & Type	Contracting Authority	Source of Funds	Estid Cost in Million Tk.	Time Code for Process	Advertise Prequal (if applicable)	Invite/ Advertise Tender	Tender Opening	Tender Evaluation	Approval of Award	Notification of Award	Signing of Contract	Total time to Contract Signature	Time for Completion of Contract
1																	
New packages																	
WD-2 (Lot-03)	Construction of Walkway and others allied work on Evicted to the North bank of Dakatia River Shekhatia Bridge to Shuchipara Bridge at Sharasti Upazila in Chandpur District.	M ³	L.S.	OTM/(NC T)	HOPE	GoB	351.28	Planned Dates	-	15-07-22	01-08-22	15-08-22	25-08-22	30-08-22	01-03-22	60 day	30-06-2023
								Planned Days	-	-	18 day	14 day	10 day	5 day	14 day		
								Actual Dates	-	-	-	-	-	-	-	-	-
							351.28										


 মোঃ আনওয়ার করিম
 নির্বাহী অফিসার
 প্রকল্প পরিচালক

ANNUAL PROCUREMENT REVISED PLAN & PROCUREMENT IMPLEMENTATION REPORT

Ministry/Division : Ministry of Shipping
 Agency : Bangladesh Inland Water Transport Authority (BIWTA)
 Procuring Entity Name & Code : Bangladesh Inland Water Transport Authority (BIWTA)
 Project/Programme Name & Code : Improvement of navigability from Mongla to Pakshi river route via Chandpur-Mawa-Gualanda (1st revised).

Package No.	Description of Procurement Package GOODS	Unit	Quantity	Procurement Method & Type	Contract Approving Authority	Source of Funds	Estid Cost in Million Tk.	Time Code for Process		Not Used in Goods	Invite/ Advertise Tender	Tender Opening	Tender Evaluation	Approval to Award	Notification of Award	Signing of Contract	Total time to Contract Signature	Time for Completion of Contract	
								9	10										
GD-04	Scanner 1 Nos	No.	01	OTM/RFQ	Project Director	GoB	0.05	Planned Dates	Actual Dates		03-07-2022	17-07-2022	31-07-2022	07-08-2022	16-08-2022	13-09-2022	72		
Total Value of Goods Procurement							0.05												

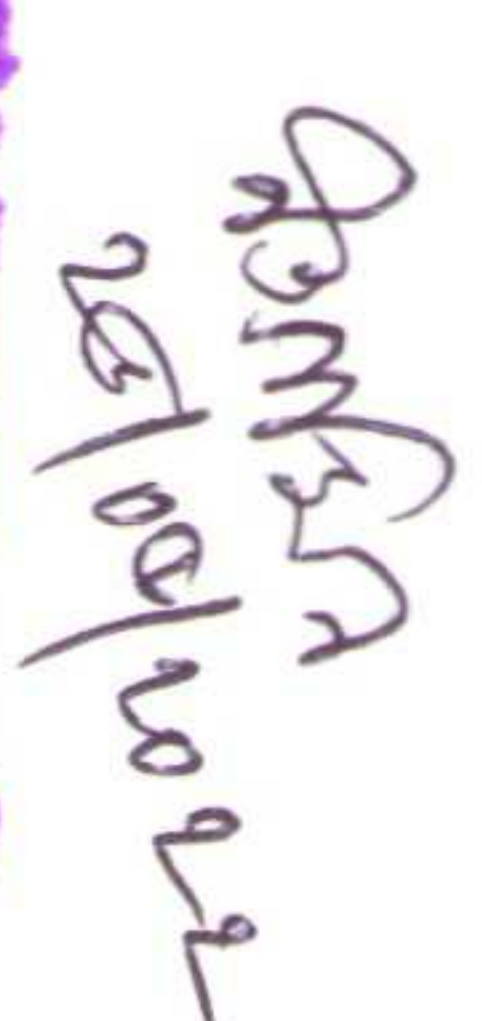
Signature
 20/08/2022
শোভা সুলতান জামিল
 উপ-পরিচালক হিসাব
 ও অতিরিক্ত দায়িত্ব
 মোংলা-পাকশি নৌ রুট প্রকল্প

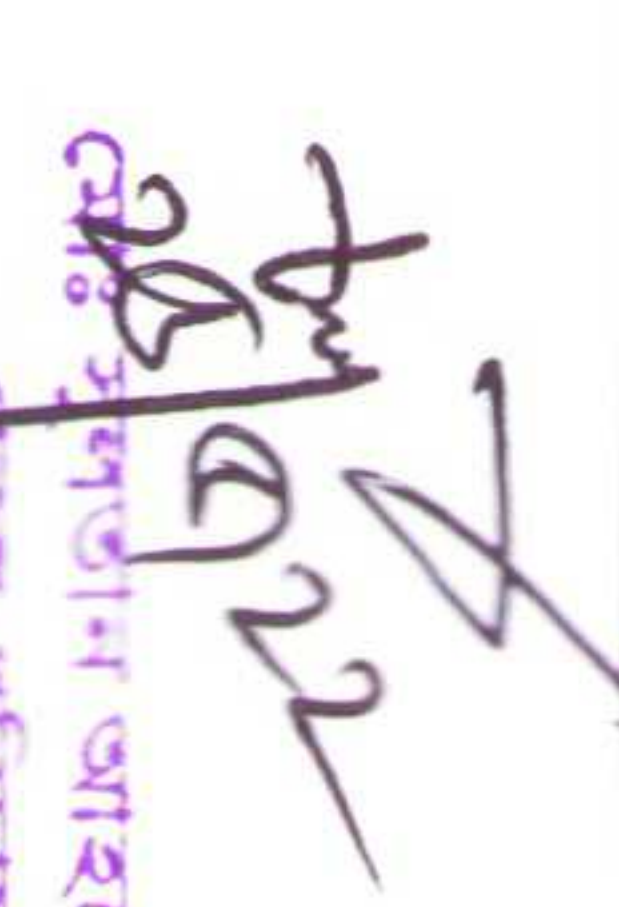
Signature
 20/08/22
শোভা সুলতান জামিল
 উপ-পরিচালক
 হিসাব ও অতিরিক্ত দায়িত্ব
 মোংলা-পাকশি নৌ রুট প্রকল্প

ANNUAL PROCUREMENT REVISED PLAN & PROCUREMENT IMPLEMENTATION REPORT

Ministry/Division : Ministry of Shipping
 Agency : Bangladesh Inland Water Transport Authority (BIWTA)
 Procuring Entity Name & Code : Bangladesh Inland Water Transport Authority (BIWTA)
 Project/Programme Name & Code : Improvement of navigability from Mongla to Pakshi river route via Chandpur-Mawa-Gualanda (1st revised).

Package No.	Description of Procurement Package WORKS	Unit	Quantity	Procurement Method & Type	Contract Approving Authority	Source of Funds	Est'd Cost in Million Tk.	Time Code for Process	Not Used in Goods	Invite/ Advertise Tender	Tender Opening	Tender Evaluation	Approval to Award	Notification of Award	Signing of Contract	Total time to Contract Signature	Time for Completion of Contract	
								9	10	11	12	13	14	15	16	17	18	
WD-2	Maintenance Dredging Works (Lot-1, Lot-2, Lot-3, Lot-4)	Lakh-M ³	160.37	DPM (Bangladesh Navy)	Cabinet committee of Government Purchase	GoB	3620.00	Planned Dates Planned Days Actual Dates		03-07-2022 0 0	24-07-2022 21	07-08-2022 14	14-08-2022 7	22-08-2022 8	20-09-2022 29	- 79	30/06/2025	
WD-3	Maintenance Dredging Works	Lakh-M ³	40.00	DPM (BIWTA)	Ministry of Shipping	GoB	600.00	Planned Dates Planned Days Actual Dates		03-07-2022	17-07-2022	31-07-2022	07-08-2022	16-08-2022	13-09-2022	-		
WD-4	Earthen Dyke (Lots of Different)	Lakh-M ³	6.67	OTM	Project Director	GoB	42.00	Planned Dates Planned Days Actual Dates		03-07-2022 0	17-07-2022 14	31-07-2022 14	07-08-2022 7	16-08-2022 9	13-09-2022 28	72		
WD-5	Bamboo Paling and torja wall (Lots of Different)	Lakh-M ²	1.00	OTM	Project Director	GoB	26.67	Planned Dates Planned Days Actual Dates		03-07-2022 0	17-07-2022 14	31-07-2022 14	07-08-2022 7	16-08-2022 9	13-09-2022 28	72		
Total Value of Works Procurement							4288.67											


 Md. Faruk
 ২৫/০৯/২২
 সিনিয়র পরিচালক
 উপ-পরিচালক হিসাব
 ও অভিবিল্ব দায়িত্ব
 মোংলা-গাকনি নৌ রুট প্রকল্প


 Md. Faruk
 ২৫/০৯/২২
 সিনিয়র পরিচালক
 উপ-পরিচালক হিসাব
 ও অভিবিল্ব দায়িত্ব
 মোংলা-গাকনি নৌ রুট প্রকল্প


**PROCUREMENT PLAN &
PROCUREMENT IMPLEMENTATION REPORT**

Budget : Development

Ministry/Division
Agency
Project/Programme Name & Code

Ministry of Shipping
Bangladesh Inland Water Transport Authority (BIWTA)
Bangladesh Inland Water Transport Authority (BIWTA)
Establishment of River Port at Chittima (Ramma, Jorgachh, Rajibpur, Rowmari, Nayaritha) & Code no-2243443

Package No.	Description of Procurement Package GOODS	Unit	Quantity	Procurement Method & Type	Contract Approving Authority	Source of Funds	Estid Cost in Million Tk.	Time Code for Process	Not Used in Goods	Invite/ Advertise Tender	Tender Opening	Tender Evaluation	Approval to Award	Notification of Award	Signing of Contract	Total time to Contract Signature	Time for Completion of Contract		
New Packages (GOODS)																			
1	১) মোটরজাহাজ ২) জীপ-১৫৫, {(রেজিষ্ট্রেশন ফি, ট্যাক্স, ভাটিক্স) এবং (সিইনোজি কনভারশন, গাউন্ডি সংক্রান্ত গাউন্ডি ও বাস্কারসহ ইত্যাদি ৩) ভারত কেরিন সিকরভাণ্ডার {(রেজিষ্ট্রেশন ফি, ট্যাক্স ও ভাটিক্স) এবং (ক্যানালি ও গাউন্ডি সংক্রান্ত গাউন্ডি ও বাস্কারসহ ইত্যাদি)}।	Nos	2	OTM	PD	GOB	12.7	Planned Dates		16-08-2022	06-09-2022	15-09-2022	22-09-2022	27-09-2022	16-10-2022	61	90 Days		
								Planned Dates			21	10	7	5	18				
								Actual Date											
2	জাহাজ (কেবিন ক্রুজার) ১টি	Nos	1	OTM	PD	GOB	15.00	Planned Dates		30-08-2022	23-09-2022	23-10-2022	02-11-2022	09-11-2022	23-11-2022	61	180 Days		
								Planned Dates			21	10	7	5	18				
								Actual Date											
3	গাড়ি	Nos	5	OTM	PD	GOB	35.00	Planned Dates		10-10-2022	02-10-2022	02-11-2022	13-11-2022	20-11-2022	06-12-2022	61	365 Days		
								Planned Dates			21	10	7	5	18				
								Actual Date											
Total Value of Goods Procurement							62.7												



স্বাক্ষর
 প্রকল্প পরিচালক
 জাহাজসংক্রান্ত
 পরিচালনা বোর্ড (পরি)
 বাংলাদেশ জাহাজসংক্রান্ত
 পরিচালনা বোর্ড

**PROCUREMENT PLAN &
PROCUREMENT IMPLEMENTATION REPORT**

Budget : Development

Ministry/Division : Ministry of Shipping
 Agency : Bangladesh Inland Water Transport Authority (BIWTA)
 Procuring Entity Name & Code : Bangladesh Inland Water Transport Authority (BIWTA)
 Project/Programme Name & Code : Establishment of River Port at Chilmari (Ramna, Jorgachh, Rajibpur, Rowmari, Navarhat) & Code no-2243443

Package No.	Description of Procurement Package WORKS	Unit	Quantity	Procurement Method & Type	Contract Approving Authority	Source of Funds	Estid Cost in Million Tk.	Time Code for Process	Advertise Prequal (if applicable)	Invite/ Advertise Tender	Tender Opening	Tender Evaluation	Approval to Award	Notification of Award	Signing of Contract	Total time to Contract Signature	Time for Completion of Contract	
New Packages (WORKS)																		
ভূমি উন্নয়ন																		
1	১) রমনা, পূর্ব কাজ-০১, স্ট-০১	m ³	0.30	OTM	PD	GOB	64.3	Planned Dates		25-08-2022	20-09-2022	20-10-2022	29-10-2022	06-11-2022	20-11-2022		360 Days	
	২) জোড়গাছ, পূর্ব কাজ-১, স্ট-০১	m ³	2.00	OTM	PD	GOB		Planned Dates				25	30	10	7	14	86	
2	ভূমি উন্নয়ন, ষ্টান জেটি নির্মাণ, যাত্রী বিদ্যামাগার, টয়লেট কমপ্লেক্স																	
	১) রাজিবপুর, পূর্ব কাজ-১২, স্ট-০১	LS		OTM	PD	GOB	Planned Dates			10-10-2020	02-10-2022	02-11-2022	13-11-2022	20-11-2022	06-12-2022		360 Days	
	২) রোমারী, পূর্ব কাজ-১৩, স্ট-০১	LS		OTM	PD	GOB	Planned Dates				22	30	11	7	16	86		
3	৩) নরারহাট, পূর্ব কাজ-১৪ স্ট-০১	LS		OTM	PD	GOB	Actual Date											
	সীমানা প্রাচীর ও বার বারবেড ওয়ারসহ																	
	১) রমনা, পূর্ব কাজ-০৩, স্ট-০১	Sqm	660		OTM	PD	GOB	Planned Dates			28-08-2022	20-09-2022	20-10-2022	29-10-2022	06-11-2022	20-11-2022		180 Days
	২) জোড়গাছ, পূর্ব কাজ-১০, স্ট-০১	Sqm	1740		OTM	PD	GOB	Planned Dates			22	30	10	7	14	83		
Total Value of Works Procurement																	138.80	



 সিনিয়র সিস্টেম এনালিস্ট
 সিস্টেম এনালিস্ট (পূর্ব)
 সিস্টেম এনালিস্ট
 সিস্টেম এনালিস্ট

**ANNUAL PROCUREMENT PLAN &
PROCUREMENT IMPLEMENTATION REPORT
2022-23**

Budget : Development

Ministry/Division : Ministry of Shipping
 Agency : Bangladesh Inland Water Transport Authority (BIWTA)
 Procuring Entity Name & Code : Bangladesh Inland Water Transport Authority (BIWTA) & 5205
 Project/Programme Name & Code : Establishment of Inland Container River Port at Ashuganj, 152- 224245900

Package No.	Description of Procurement Package (WORKS)	Unit	Quantity	Procurement Method & Type	Contract Approving Authority	Source of Funds	Est'd Cost in Lakh Tk.	Time Code for Process	Advertise Prequel (if applicable)	Invite/ Advertise Tender	Tender Opening	Tender Evaluation	Approval of Award	Notification of Award	Signing of Contract	Total time to Contract Signature	Time for Completion of Contract
WD-01	Construction of Infrastructural facilities (Civil & related items) (Proposed as per RDPP)	Each	Each	OTM (ICT) International by Indian Contractor)	CCGP	DPA (LoC & Gob)	70900.00 (Proposed as per RDPP)	Planned Dates	-	01-08-2022	11-09-2022	09-10-2022	19-10-2022	24-10-2022	07-11-2022	99 day	Dec/24
							Total =	Actual Dates	-	-	-	-	-	-	-	-	-
							70900.00										


 06.08.2022
(Md. Shajadur Rahman)
 Superintending Engineer,
 Dhaka Circle, BIWTA,
 Project Director


ANNUAL PROCUREMENT REVISED PLAN & PROCUREMENT IMPLEMENTATION REPORT

Budget: Development
Year: 2022-2023

Ministry / Division : Ministry of Shipping
 Agency : Bangladesh Inland Water Transport Authority (BIWTA)
 Procuring Entity Name & Code : Bangladesh Inland Water Transport Authority (BIWTA)
 Project/Programmed Name & Code : "Construction & Installation of demarcation pillar, Walkway, Bank Protection, Jetty with allied work on Evicted Foreshore Land of the River Buriganga, Turag, Balu and Sitalakhya (2nd Phase) (1st Revised)".

Project Code: 224245700

Package No	Description of Procurement Package WORKS	Unit	Quantity	Procurement Method & Type	Contract Approving Authority	Source of Funds	Est'd Cost in Million Tk.	Time Code for Process		Advertise Prequel (if applicable)	Invite/ Advertise Tender	Tender Opening	Tender Evaluation	Approval to Award	Notification of Award	Signing of Contract	Total time to Contract Signature	Time for Completion of Contract	
								Planned Dates	Actual Dates										
1	New Package																		
RWD-18	ঢাকা, টাঙ্গী ও নারায়ণগঞ্জ নদী বন্দরের নদীর তীরবর্তীতে জনস্বত্বভঙ্গনকারী সাইনবোর্ড স্থাপন কাজ। (একসিক বর্ড)	Nos	76	LTM	PD	GOB	137.79	Planned Dates	Actual Dates	---	15-Jul-22	05-Aug-22	20-Aug-22	09-Sep-22	16-Sep-22	14-Oct-22	28 days	91 days	210 days
RWD-29	ঢাকা, টাঙ্গী ও নারায়ণগঞ্জ নদী বন্দরের তীরবর্তীতে বিভিন্ন স্থানে বিভিন্ন প্রকারের বৃক্ষরোপণ কাজ। (একসিক বর্ড)	Meter	-	OTM	PD	GOB	340.10	Planned Dates	Actual Dates	---	15-Jul-22	12-Aug-22	27-Aug-22	16-Sep-22	23-Sep-22	21-Oct-22	28 days	98 days	210 days
Total Value of Works Procurement =							477.89												

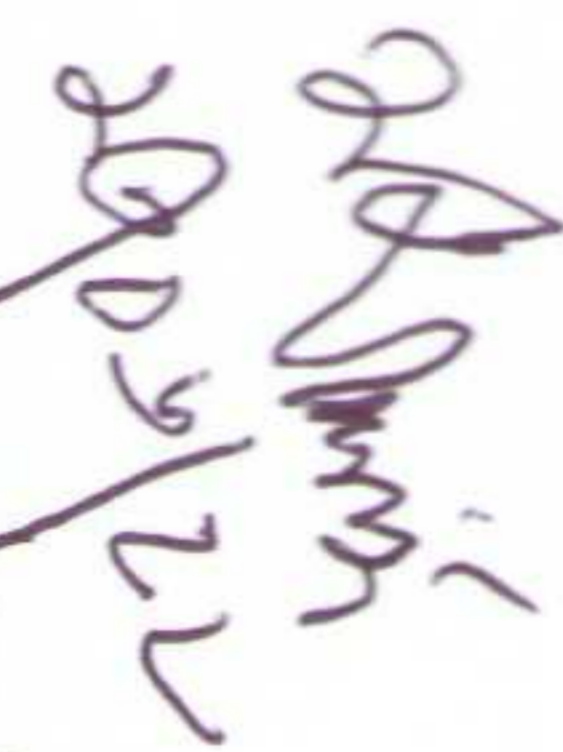

 (আবু আব্দুল মোমেন শাহজাদেজাজ করিম)
 ডায়াক্টর এক্সিকিউটিভ (অস)
 জেজিইসি, বিআইডব্লিউটিএ, ঢাকা
 ৯
 স্বাক্ষর পরিচালক

ANNUAL PROCUREMENT REVISED PLAN & PROCUREMENT IMPLEMENTATION REPORT

Budget : Development

Ministry/Division : Ministry of Shipping
 Agency : Bangladesh Inland Water Transport Authority (BIWTA)
 Procuring Entity Name & Code : Bangladesh Inland Water Transport Authority (BIWTA)
 Project/Programme Name & Code : Determination of Standard High Water Level (SHWL), Standard Low Water Level (SLWL) and Re-Classification of Inland Waterways in Bangladesh & Code : 224345400

Package No.	Description of Procurement Package	Unit	Qty	Procurement Method & Type	Contract Approving Authority	Source of Funds	Esid Cost in Million Tk	Time Code for Process	Not Used in Goods	Invite/ Advertise Tender	Tender Opening	Tender Evaluation	Approval to Award	Notification of Award	Signing of Contract	Total time to Contract Signature	Time for Completion of Contract
1	GOODS	3	4	5	6	7		9	10	11	12	13	14	15	16	17	18
GD3	ArcGis and Oracle software	No	2	OT M	Chairman BIWTA	GOB	18.00	Planned Dates		21.08.22	04.09.22	18.09.22	02.10.22	09.10.22	07.11.22	77	30.06.23
								Planned Dates		0	14	14	14	7	28		
								Actual Date									
GD4	Water Resources (20 years Water Level Data) and Bench Mark Value	No	402	DPM, Multipul Source (BWDB, CPA, MPA, WARPO, SOB)	Chairman BIWTA	GOB	1.21	Planned Dates		17.07.22	01.08.22	14.08.22	28.08.22	04.09.22	02.10.22	77	30.06.23
								Planned Days		0	14	14	14	7	28		
								Actual Date									
Total Value of Goods Procurement							19.21										


 20/09/22
 (স্বাঃ. আফগানিস্তান উদ্দেশ্যে)
 যুগ্ম-পরিচালক (টাইড) ভারতীয়
 হাইড্রোগ্রাফিক বিভাগ, বাআসীপক, ঢাকা
 ৩
 প্রকল্প পরিচালক।


ANNUAL PROCUREMENT REVISED PLAN & PROCUREMENT IMPLEMENTATION REPORT

Budget: Development
Year: 2022-2023

Ministry / Division : Ministry of Shipping
Agency : Bangladesh Inland Water Transport Authority (BIWTA)
Project/Programmed Name & Code : Bangladesh Inland Water Transport Authority (BIWTA)
Project/Programmed Name & Code : "Construction & Installation of demarcation pillar, Walkway, Bank Protection, Jetty with allied work on Evicted Foreshore Land of the River Buriganga, Turag, Balu and Sitalakhya (2nd Phase) (1st Revised)".

Project Code: 224245700

Package No	Description of Procurement Package WORKS	Unit	Quantity	Procurement Method & Type	Contract Approving Authority	Source of Funds	Est'd Cost in Million Tk.	Time Code for Process	Advertise Prequel (if applicable)	Invite/ Advertise Tender	Tender Opening	Tender Evaluation	Approval to Award	Notification of Award	Signing of Contract	Total time to Contract Signature	Time for Completion of Contract
1	New Package																
RWD-18	ঢাকা, টঙ্গী ও নারায়ণগঞ্জ নদী বন্দরের নদীর তীরভূমিতে জনসচেতনতামূলক সার্বজনিক স্থাপন কাজ। (একাধিক লট)	Nos	76	LTM	PD	GOB	137.79	Planned Dates	---	15-Jul-22	05-Aug-22	20-Aug-22	09-Sep-22	16-Sep-22	14-Oct-22	91 days	210 days
RWD-29	ঢাকা, টঙ্গী ও নারায়ণগঞ্জ নদী বন্দরের অধীনে বিভিন্ন স্থানে বিভিন্ন প্রকারের বৃক্ষরোপণ কাজ। (একাধিক লট)	Meter	-	OTM	PD	GOB	340.10	Planned Dates	---	15-Jul-22	12-Aug-22	27-Aug-22	16-Sep-22	23-Sep-22	21-Oct-22	98 days	210 days
Total Value of Works Procurement =							477.89										


 (আবু জাফর মোহাম্মদ শহিদুল্লাহ করিম)
 তত্ত্বাবধায়ক প্রকৌশলী (জঃ)
 জেজিইবিআপ, বিআইভিউটিএ, ঢাকা
 স্বাক্ষর পরিচালক

Ministry/Division
Agency
Procuring Entity Name & Code
Project/Programme Name & Code

Ministry of Shipping
Bangladesh Inland Water Transport Authority (BIWTA)
Bangladesh Inland Water Transport Authority (BIWTA)
Establishment of Dhaka-Laksmipur Navigational route on Meghna (lower) River & Code No.- 224307600

ANNUAL PROCUREMENT REVISED PLAN & PROCUREMENT IMPLEMENTATION REPORT

Budget : Development

Package No.	Description of Procurement Package WORKS	Unit	Quantity	Procurement Method & Type	Contract Approving Authority	Source of Funds	Estid Cost in Million Tk.	Time Code for Process		Advertise Prequel (if applicable)	Invite/ Advertise Tender	Tender Opening	Tender Evaluation	Approval to Award	Notification of Award	Signing of Contract	Total time to Contract Signature	Time for Completion of Contract
								9	10									
WD-04	Ancillary Work and Construction of earthen dyke.	per Cum	8.00	OTM	PD	GOB	14.399	Planned Dates			03/07/2022	18/07/2022	08/08/2022	21/08/2022	29/08/2022	01/09/2022	-	30/06/2023
								Planned Dates			-	15	13	13	8	3	52	-
								Actual Dates										
WD-03	Construction of Tarja wall	m2	7000	OTM	PD	GOB	2.10	Planned Dates			03/07/2022	18/07/2022	08/08/2022	21/08/2022	29/08/2022	01/09/2022	-	30/06/2023
								Planned Dates			-	15	13	13	8	3	52	-
								Actual Dates										
Total Value of Works Procurement							16.499											


23/06/2023


(আব্দুর রব সজ্জা)
নির্বাহী প্রকৌশলী (প্র)
ক্রয় বিভাগ, বাআনৌপক, ঢাকা
প্রকল্প পরিচালক

**ANNUAL PROCUREMENT PLAN &
PROCUREMENT IMPLEMENTATION REPORT
FOR THE YEAR 2022-2023**

Budget : Development

Ministry/Division : Ministry of Shipping
 Agency : Bangladesh Inland Water Transport Authority (BIWTA)
 Procuring Entity Name & : Bangladesh Inland Water Transport Authority (BIWTA)
 Code No. : 15205
 Project/Programme Name & : "Establishment of River Port with allied facilities at Nagarbari (1st Revised)".
 Code No. : 224236500

Package No.	Description of Procurement Package GOODS	Unit	Quantity	Procurement Method & Type	Contract Approving Authority	Source of Funds	Estid Cost in Million Tk.	Time Code for Process		Not Used in Goods	Invite/ Advertise Tender	Tender Opening	Tender Evaluation	Approval to Award	Notification of Award	Signing of Contract	Total time to Contract Signature	Time for Completion of Contract
								9	10									
G-3	Procurement of 02 Nos. Mobile Harbor Crane, 01 No. Fork Lift & 01 No. Convoy Velt at Nagarbari under the project of "Establishment of River Port with allied facilities at Nagarbari (1st Revised)".	NOS	4	OTM	MoS	GoB	406.00	Planned Dates	-	05-10-22	09-11-22	07-12-22	14-12-22	21-12-22	18-01-23	-	-	27-06-2023
								Planned Dates	-	-	35 day	28 day	7 day	7 day	28 day	105 days	-	-
								Actual Date	-	-	-	-	-	-	-	-	-	-
G-4	Purchase of furniture for use in various infrastructures at Nagarbari under the project of "Establishment of River Port with allied facilities at Nagarbari (1st Revised)".	LS	LS	OTM	PD	GoB	5.0	Planned Dates	-	19-10-22	15-11-22	13-12-22	20-12-22	27-12-22	25-01-23	-	-	25-06-2023
								Planned Dates	-	-	27 day	28 day	7 day	7 day	29 day	98 days	-	-
								Actual Date	-	-	-	-	-	-	-	-	-	-
Total Value of Goods Procurement							411.00											

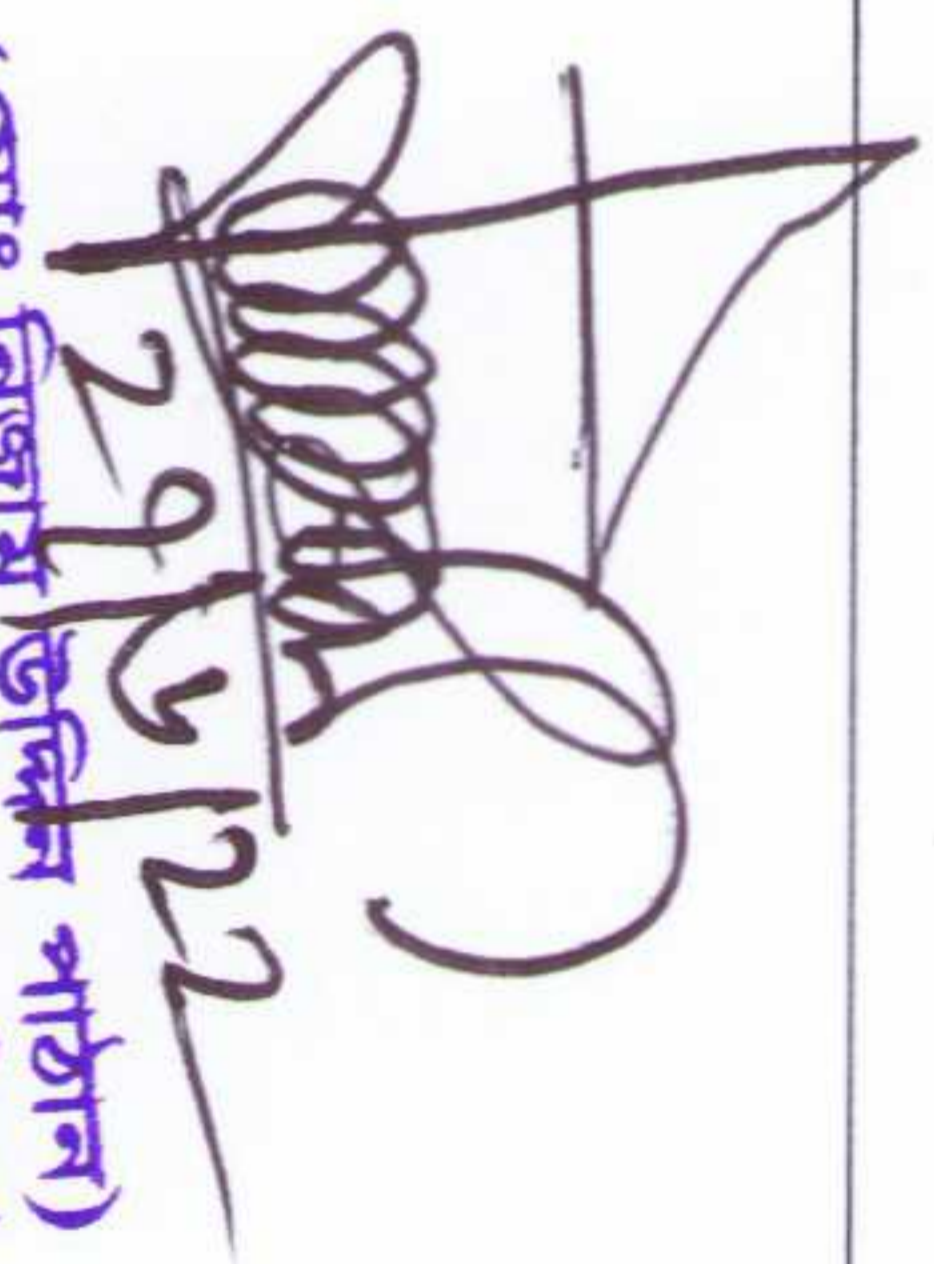

 (স্বাঃ নিজাম উদ্দিন পাঠান)
 নির্বাহী প্রকৌশলী, প্রকৌশল বিভাগ
 প্রকল্প কাজে নিয়োজিত কর্মকর্তা।

**ANNUAL PROCUREMENT PLAN &
PROCUREMENT IMPLEMENTATION REPORT
FOR THE YEAR 2022-2023**

Budget : Development

Ministry/Division : Ministry of Shipping
Agency : Bangladesh Inland Water Transport Authority (BIWTA)
Procuring Entity Name & : Bangladesh Inland Water Transport Authority (BIWTA)
Code No. : 15205
Project/Programme Name & : "Establishment of River Port with allied facilities at Nagarbari (1st Revised)".
Code No. : 224236500

1	Description of Procurement Package WORKS	Unit	Quantity	Procurement Method & Type	Contract Approving Authority	Source of Funds	Est'd Cost in Million Tk.	9		10	11	12	13	14	15	16	17	18
								Time Code for Process	Advertise Prequel (if applicable)									
W-8	Construction of 06 Nos. Godown (Warehouse), 03 Nos. Open shedded Warehouse and 01 No. Workshop at Nagarbari under the project of "Establishment of River Port with allied facilities at Nagarbari (1st Revised)".	Sqm	14582.00	OTM	Mos	GoB	431.50	Planned Dates	-	15-07-22	14-08-22	11-09-22	18-09-22	25-09-22	23-10-22	100 days	29-06-2023	
W-14	Dredging Work by Cutter Suction Dredger in Channel and Basin in front of Nagarbari Port Area at Nagarbari under the project of "Establishment of River Port with allied facilities at Nagarbari (1st Revised)".	Cum	12 lakh	OTM	HOPE	GoB	216.00	Planned Dates	-	10-10-22	16-11-22	12-12-22	19-12-22	26-12-22	23-01-23	105 days	27-06-2023	
W-15	Installation of Fire Fighting System Over the Whole Port Area at Nagarbari under the project of "Establishment of River Port with allied facilities at Nagarbari (1st Revised)".	LS	LS	OTM	PD	GoB	30.0	Planned Dates	-	17-07-22	21-08-22	20-09-22	27-09-22	04-10-22	03-11-22	109 days	28-06-2023	
W-17	Gardening & Beautification works Over the Whole Port Area at Nagarbari under the project of "Establishment of River Port with allied facilities at Nagarbari (1st Revised)".	LS	LS	OTM	PD	GoB	5.0	Planned Dates	-	19-10-22	09-11-22	07-12-22	14-12-22	21-12-22	18-01-23	91 days	25-06-2023	
Total Value of Works Procurement							682.50											



 (স্বাঃ নিজাম উদ্দিন পাঠান)
 নির্বাহী প্রকৌশলী, প্রকৌশল বিভাগ
 প্রকল্প কাজে নিয়োজিত কর্মকর্তা।

**ANNUAL PROCUREMENT PLAN &
PROCUREMENT IMPLEMENTATION REPORT
FOR THE YEAR 2022-2023**

Budget : Development

Ministry/Division : Ministry of Shipping
Agency : Bangladesh Inland Water Transport Authority (BIWTA)
Procuring Entity Name & Code No. : Bangladesh Inland Water Transport Authority (BIWTA) 15205
Project/Programme Name & Code No. : "Establishment of Inland Container and Bulk Terminal at Khanpur, Narayanganj". 224353100

Package No.	Description of Procurement Package SERVICES	Unit	Quantity	Procurement Method & Type	Contract Approving Authority	Source of Funds	Est'd Cost in Million Tk.	Time Code for Process		Avestise EOI	Issue RFP	Technical Proposal opening	Technical Proposal Evaluation	Financial Proposal opening & Evaluation	Negotiation	Approval	Signing of Contract	Total time to Contract Signature	Time for Completion of Contract
								9	10										
S-1	Consultancy Services for Detailed Design of Architectural, Equipment & Utilities including Cost Estimate and Construction Supervision for the Project of "Establishment of Inland Container and Bulk Terminal at Khanpur, Narayanganj".	LS	LS	QCBS	MoS	GoB	266.60	Planned Dates	-	-	-	20-07-2022	21-08-2022	12-09-2022	27-09-2022	12-10-2022	10-11-2022	-	1520 day
								Planned Dates	-	-	-	73 day	32 day	22 day	15 day	15 day	29 day	260 day	-
								Actual Dates	23-02-22	08-05-2022	-	-	-	-	-	-	-	-	-
Total Value of Service Procurement							266.60												


 (স্বঃ নিজাম হুসাইন পাঠান)
 নির্বাহী অফিসার
 ২৭/১২/২২
 প্রকল্প পরিচালক।
